



Rio De Flag, AZ

Construction

U.S. ARMY CORPS OF ENGINEERS

BUILDING STRONG.

LOCATION AND DESCRIPTION:

This flood risk management project is located in and near the city of Flagstaff, Coconino County, Arizona. The area is subject to flooding from Rio de Flag and Clay Avenue Wash tributaries.

The plan consists of channel modifications, bridge enhancements, detention basin construction, and floodwall construction.

AUTHORIZATION:

WRDA 2000 Sec 101 (b) (3), WRDA 2007, Sec. 3007.

ACTIVITIES FOR FY 2021: Funds are being used to complete 100% Design for the Rio de Flag project, conduct Agency Technical Review (ATR), and Safety Assurance Review (SAR). Coordination with BNSF Railways is ongoing for the two Construction Management Agreements (CMA) one for undercrossing, and the other for the Lower Reach portion. Contract award planned for SEP 2020 for the Lower Reach and Clay Ave Reach is delayed – Real Estate needs re-appraisal.

FY 2022 PLANNED ACCOMPLISHMENTS:


First contract Lower Reach and Clay Ave Reach contract award now anticipated March 2022. Second contract of Upper Reach anticipated September 2022.

ISSUES AND OTHER INFORMATION: The LRR was completed and new total project cost of \$102.8M included in WRDA 2016 (WIIN 2016).

BNSF issue: The plan to is to move forward with the two CMA's – one for the undercrossing (Tunneling option being the most favorable); and one CMA for the Lower Reach. Discussions are still on-going between the Corps, City and BNSF to align the Real Estate on time for construction. **Real Estate issue:** Will need to be re-appraised by Sponsor. PDT working with Sponsor to provide clarity of steps.

CONGRESSIONAL INTEREST:

Senators; Kelly and Sinema, and Congressman O'Halleran (AZ-1), and Congressman Gosar (AZ-4).

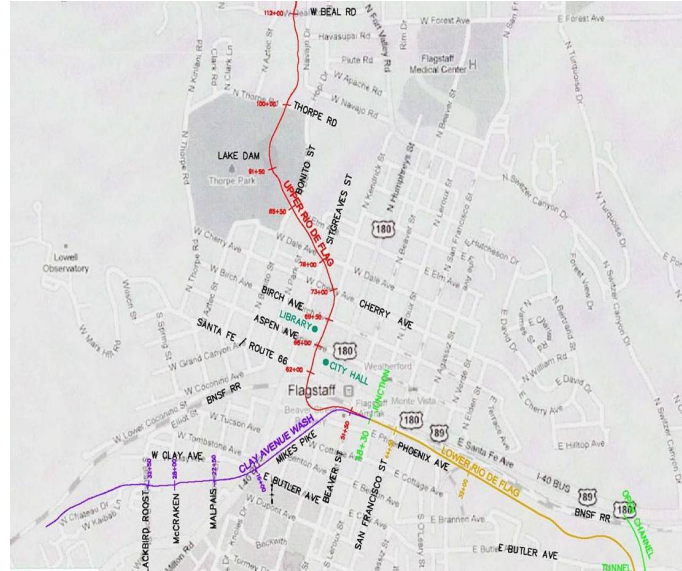

As of: 1 Mar 21

SUMMARIZED FINANCIAL DATA:

	<u>Construction</u>
Estimated Federal Cost	\$79,516,000
Estimated Non-Federal Cost	\$42,334,000
Total Estimated Project Cost	\$121,850,000
Allocation thru FY20	\$79,516,000
Allocations for FY21	\$0
President's Budget for FY22	0
House Report for FY22	0
Senate Report for FY22	0
Balance to Complete After FY22	\$0

U.S. ARMY CORPS OF ENGINEERS – LOS ANGELES DISTRICT

915 WILSHIRE BLVD., SUITE 930, LOS ANGELES, CA 90017

<http://www.spl.usace.army.mil>
