




Tucson Drainage Area, AZ

Construction

U.S. ARMY CORPS OF ENGINEERS

BUILDING STRONG.

LOCATION AND DESCRIPTION: The project consists of flood control and ecosystem restoration which measures within the approximate 12-square mile of Tucson Arroyo/Arroyo Chico watershed in the City of Tucson located in Pima County, Arizona. The authorized project consists of two detention basin complexes. One referred to as the Randolph Golf Course Detention Basin complex (upstream on Arroyo Chico in the headwaters of the drainage), and the second referred to as the Park Avenue Basin complex (in the approx. center of the watershed). The local sponsor pursued and was granted consideration of the 104 credits in advance of completion of the feasibility phase. The Randolph Detention Basin complex was completed in May 1996

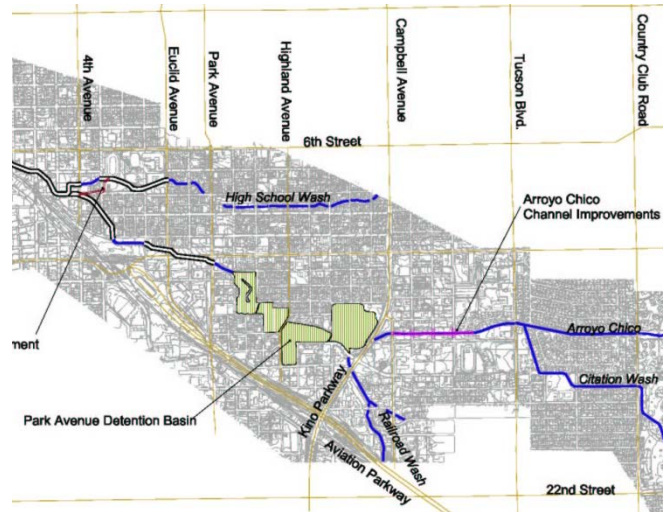

AUTHORIZATION: WRDA 1999, Sec 101(a) (5); WRDA 2007 Sec 3009

ACTIVITIES FOR FY 2017: Conducted Mapping Survey, and Geotechnical & Environmental testing and characterization within a ¾ mi long segment of Arroyo Chico Wash, in support of planned channel construction to relief bottleneck constriction in upstream wash segment of project

FY18 PLANNED ACCOMPLISHMENTS: Develop bid packages for Increment 3 and award for construction. Additional work will include environmental review and update of project documents to satisfy environmental commitments, and, project close-out.

ISSUES AND OTHER INFORMATION: Increment 3 was de-scoped from contract and funds were utilized for mods on Increment 4. Estimated funds need to complete project in FY18 include \$4.5M for construction of wash channel features to improve conveyance and reduce potential breakout flooding during storm events; Additional funding package of \$500K is needed - \$250K to conduct analysis and write-up in support of Environmental Assessment (EA) commitments; and, additional \$250K for project close-out.

As of: 23 Mar 17

SUMMARIZED FINANCIAL DATA:

Construction

Estimated Federal Cost	\$42,887,000
Estimated Non-Federal Cost	\$23,093,000
Total Estimated Project Cost	\$65,980,000
Allocation thru FY16	\$38,442,000
Allocations for FY17	0
President's Budget for FY18	TBD
House Report for FY18	TBD
Senate Report for FY18	TBD
Balance to Complete After FY18	\$4,445,000

CONGRESSIONAL INTEREST: Congresswoman McSally (AZ-2), Congressman Grijalva (AZ-3) & Gallego (AZ-7)

U.S. ARMY CORPS OF ENGINEERS – LOS ANGELES DISTRICT

915 WILSHIRE BLVD., SUITE 930, LOS ANGELES, CA 90017

<http://www.spl.usace.army.mil>
